WORLDWIDE POWER PRODUCTS

Load Test Report

Account Name:

Asset Location (Service Address): 5711 Brittmoore Rd.

Asset: 7291

	Engine	Generator
Man.		
Model		

Engine Fluids:

Engine Fluids:	
Ok	Oil Level
Ok	Coolant Level
100%	Starting Fuel Level
	Ending Fuel Level

Load Test Reports

Serviceperson:		
James M	Test Date	21-May-20
	Time In	1:00 PM
	Time Out	2:05 PM
	Total Time:	

Test Equipment

Make	
Model	
Serial #	

Load Step (kW/min)	Time	Hour Meter	Volt Meter	Frequency (Hz)	Power (kW)	Leg A Amps	Leg B Amps	Leg C Amps	Oil Press (PSI)	Water Temp (F)	Ambient Temp
5/30	1:00 PM	11030	480	60	0	0	0	0	70	120	90
	1:15 PM	11031	480	60	15	18	18	18	48	188	90
	1:30 PM	11031	480	60	25	31	31	31	45	188	90
	1:45 PM	11031	480	60	40	49	49	49	40	192	90
	2:00 PM	11031	480	60	56	68	68	68	35	204	90
	2:05 PM	11031	480	60	0	0	0	0	70	120	90

Account Name:

5711 Brittmoore Rd.
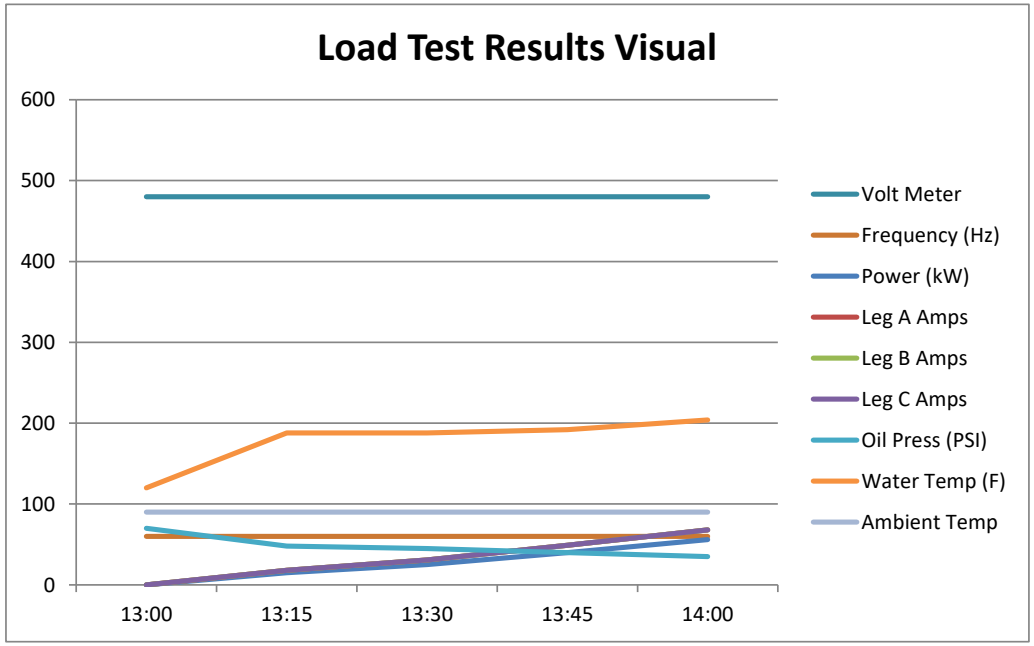
Work Order:
